







# CONSTRUCTION UPDATES

MARCH 8, 2024

JASPREET PAHWA, NCARB, LEED AP DIRECTOR, CAPITAL PLANNING & CONSTRUCTION DC PUBLIC LIBRARY

### **Reminders**

- Hours of Work:
  - Permitted Hours: Monday Saturday (7am 7pm)
  - Projected Workday: Monday Saturday (7am 5pm)
- Link to the recording from December 14, 2023 Pre-Construction Community Meeting hosted at the Southeast library for the broader Community
- Link to the presentation from December 14, 2023 Pre-Construction Community Meeting
- Link to the Construction Sequence video presented by Whiting-Turner

#### NOTE:

Traffic Control measures in place supersede the plan shown and shared on December 14, 2023 - Reference slide 4 of this update.



## Pedestrian Safety Measures Discussed Onsite w/ DDOT March 6, 2024


Attendees: Library, Whiting-Turner, DDOT, ANC Commissioner, Taskforce members & Neighbors Here is the <u>Link</u> to the letter issued by ANC Transportation Committee to DDOT on February 22, 2024 Action items from Meeting:

- 7th Street Traffic Pattern DDOT to provide analysis to ANC. No action item for Library or WT.
- **D St Temporary Crosswalk** Library directed WT to install the temporary mid-block crosswalk per direction from DDOT.
- South Carolina Pedestrian Path Requires engineering coordination including design of a temporary ADA ramp. Library is enabling this through Civil Engineer of Record for the project to ultimately seek a revised Traffic Control Plan from DDOT.
- Scrim on fencing for improved pedestrian/traffic sight-lines In discussion w/ DDOT, WT has peeled back scrim from 2 additional panels.





#### **Traffic Control Measures Currently in Place** Will change following coordination w/ DDOT

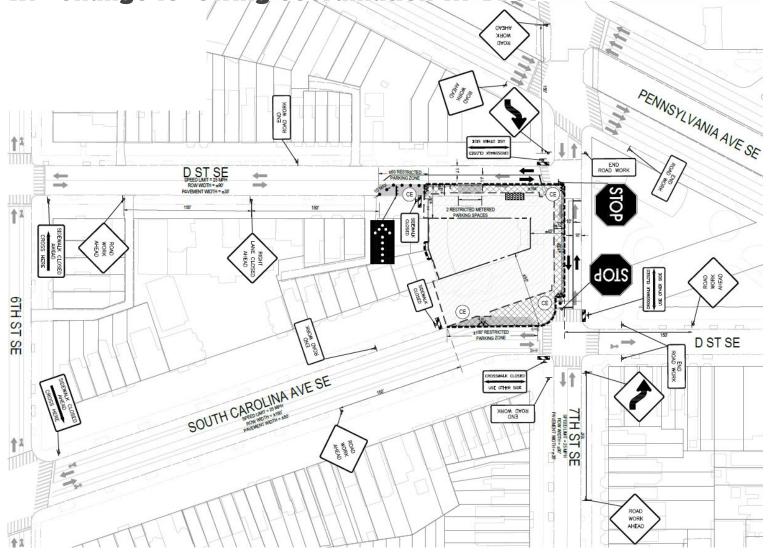





Safety mirror installed on 7th Street



Scrim from 2 additional panels removed for pedestrian & vehicular safety on March 7, 2024





### **Construction Progress - Main Floor**



**Ceiling Stripped Interior Walls Exposing Terracotta and Brick** 

Demolition of Existing Plaster Ceiling to Expose Historic Laylight that will be Restored



#### **Construction Progress - Lower Floor**



Plaster Ceiling Removed & Concrete Slab Exposed



### **Construction Progress - Floor and Wall Demolition**



**Demolition of Existing Walls underway** 

**Demolition of Concrete Slab underway** 



## **Construction Progress - Elevator Demolition**



Demolition of Existing Elevator & Shaft



#### **One Month Look Ahead**

- Installation of mid-block crosswalk & DDOT required street signage on D St
- Initiate revision of Traffic Control Plan via DDOT for pedestrian path on South Carolina Ave.
- Completion of lower level Interior slab demolition
- Completion of exterior retaining wall demolition Noisy work similar to previous weeks
- Exterior earthwork removal at the berm
- Haul-off old equipment, exterior railings, old fence, generator
- Start installation of Interior structural steel to enable demolition of old load bearing walls
- Start underpinning along adjoining walls of Townhomes and existing Library Wall on D Street late March
  - WT will maintain contact with the 2 adjoining neighbors and monitor vibration readings
- No watermain replacement or shut-off expected in the next 4 weeks
- No lane closures projected but an uptick projected in Construction Trucks on D Street and South Carolina Ave



# **Let's Stay Connected**

#### **Periodic Construction Updates & Notifications from DC Public Library**

By: Director, Capital Planning & Construction, Jaspreet Pahwa

Next update in approximately 4 weeks

#### **Time-Sensitive Construction Safety Issues**

Superintendent, Nathan Shields: 443-900-2117

#### **General Questions**

Email, Director, Community Engagement: Martha.Saccocio@dc.gov

### Additionally:

Library & Whiting-Turner Construction leads in attendance at the ANC hosted Library Taskforce meeting on Jan 21,& Feb 19, 2024. Team plans to attend the future Taskforce meetings in lieu of presenting construction updates at the ANC meetings.

